TN OF ALGOMA - BELLHAVEN SAND FILTER
CONSTRUCTION SCHEDULE

NORTHEAST ASPHALT
J.PHILLIPS
Mon 6/3/24
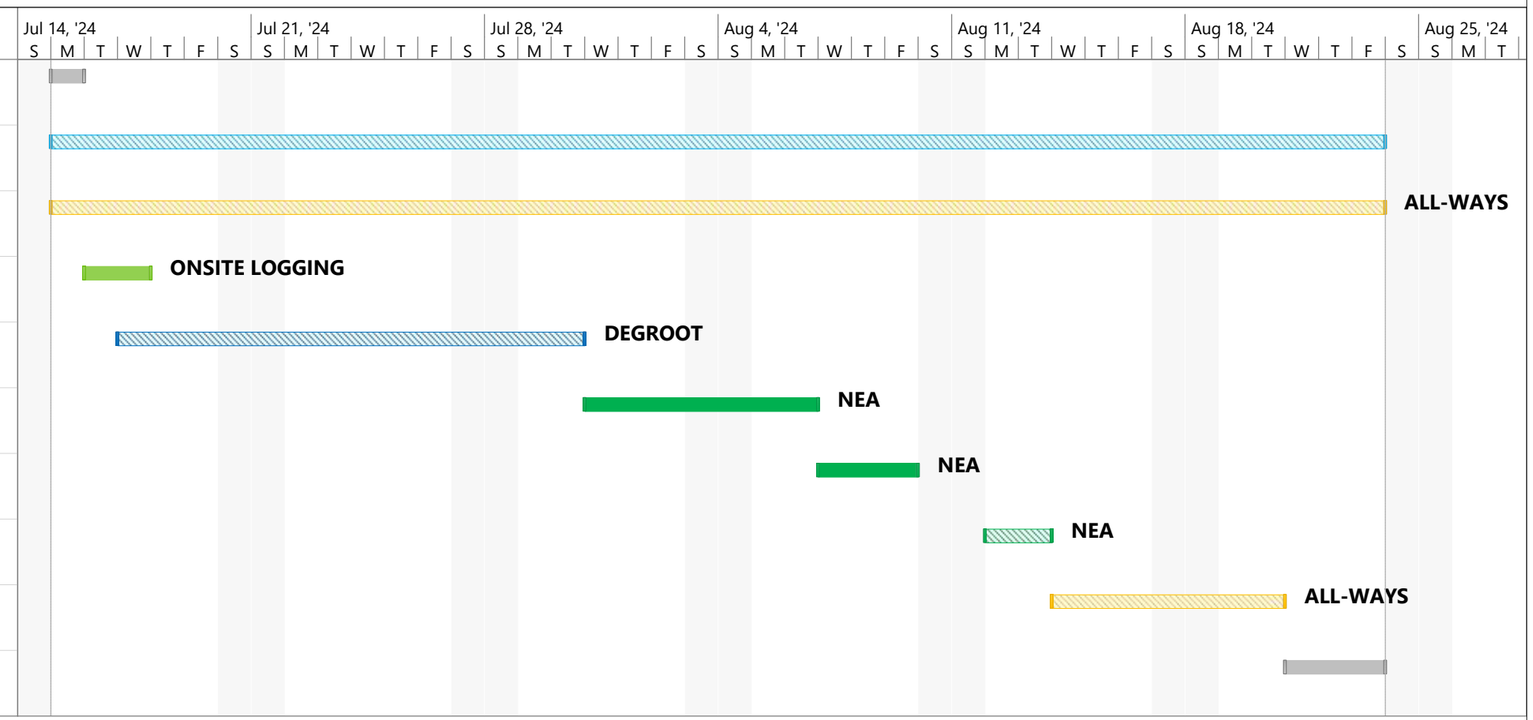
ID	Task Name	Duration	Start	Finish	Resource Names
1	MOBILIZATION	1 day	Mon 7/15/24	Mon 7/15/24	
2	TRAFFIC CONTROL	30 days	Mon 7/15/24	Fri 8/23/24	
3	EROSION CONTROL	30 days	Mon 7/15/24	Fri 8/23/24	ALL-WAYS
4	CLEAR AND GRUB	2 days	Tue 7/16/24	Wed 7/17/24	ONSITE LOGGING
5	STORM SEWER	10 days	Wed 7/17/24	Tue 7/30/24	DEGROOT
6	POND EXCAVATION	5 days	Wed 7/31/24	Tue 8/6/24	NEA
7	SAND/IRON/PEA GRAVEL	3 days	Wed 8/7/24	Fri 8/9/24	NEA
8	ASPHALT PATCHING	2 days	Mon 8/12/24	Tue 8/13/24	NEA
9	LANDSCAPING	5 days	Wed 8/14/24	Tue 8/20/24	ALL-WAYS
10	CLEAN UP/PUNCHLIST	3 days	Wed 8/21/24	Fri 8/23/24
